# MATJHABENG MUNICIPALITY

# **ANNEXURES**

of the

# 5<sup>TH</sup> SPECIAL COUNCIL MEETING

convened for

WEDNESDAY, 01 NOVEMBER 2017

at

15:00

at the

COUNCIL CHAMBERS, CIVIC CENTRE, WELKOM

## MATJHABENG

#### MUNICIPALITY MMASEPALA



#### UMASIPALA MUNISIPALITEIT

10.	DISCUSSION	ACTION	
	OPENING AND WELCOME  Mr. Mohlabane declared the meeting officially opened and welcomed all present.		
•	The following were in attendance:  - Matoli S Matjhabeng Municipality - Saru L.I - Human Settlements - Porotloana M.C - Matjhabeng Municipality - Mohlabane S.J - Human Settlements - Funani N.N - VNA Consulting - Sephton W.E - Matjhabeng Municipality - Ramona S.M - Matjhabeng Municipality - Sello L - Matjhabeng Municipality - Mohapi T Matjhabeng Municipality - L. Sello - Matjhabeng Municipality - Mashele L NWA Mencani Trading - Molelekoa B.K - Matjhabeng Municipality - Mieuwouldt F Matjhabeng Municipality		
	APOLOGIES  Me Cecilia Porotloana excused herself from the meeting to attend to family emergency.	Noted by members	
<b>.</b>	<b>INTRODUCTION</b> The chairperson requested everybody present to introduce themselves accordingly. See attendance.		
i.	PURPOSE OF THE MEETING  The chairperson indicated that the purpose of the meeting was to determine the land readiness for the development of the 100 subsidized Integrated Housing Development in Ventersburg in order that the contractor could carry on with construction.  Agenda  Electricity Water	Noted members.	
	could carry on with construction.  Agenda		

#### 5.1 ELECTRICITY

Mr. Sephton Sephton reported that the capacity for that specific area was 1390kva of which only 40kva was available and can only be connected to one subsidized house.

He also indicated that the cable was also too small and needs R800 000.00 to be upgraded. He said that the quotation he drafted is for the 75 sites which are already existing reflected as follows;

- R 2 850 000.00 for Upgrading of NMD at Ventersburg Municipal/Eskom.
- R 1 998 640.00 for Provision and installation of 35mm<sup>2</sup> x 3 Core PILC copper cable.
- R 841 320.00 for Provision and installation of 60mm<sup>2</sup> x 3 Core MINK overhead line between Hamilton and Eskom Ventersburg Municipal Intake point
- R 3 156 795.00 for Provision and installation of 60 Amp 220Volt Single Phase Connections to Stand.
- Total funds required R 11 598 095.81

He advised the meeting that for the envisaged 100 sites the figures will change drastically and that it needed to be taken into account that the area was previously advantaged and could not receive any funds like MIG etc. That Mr Mr. Sephton Sephton to draft a revised quotation and submit to Mr Sello of human settlements for circulation to stakeholders.

#### 5.2 WATER AND SEWER

Mr. Nieuwouldt reported that he was not sure as to whether water and sewer pipes were available in that particular land. Mr. Nieuwouldt was subsequently requested to seek information regarding what services are currently there, what services are required, how long it will take to put those services and how much it will cost.

The contractor, NWA alluded that the lack of services will cause a further delay and might affect the department's goal to meet the target in terms of construction of houses within the current financial year.

- That Mr. Nieuwouldt to acquire information regarding the existence of water and sewer services and submit information to Mr. Sello by Wednesday 06 September 2017. Mr. Sello for circulation to stakeholders.
- That VNA to write a letter to the Chief Director Technical Services regarding all the challenges outlined in the meeting as well as the information to be provided by Mr. Nieuwouldt.

#### 5.3 BENEFICIARIES

Me Sweetness Ramona informed the meeting that 201 black and white beneficiaries were verified and that 37 whites and 40 blacks qualified. She further explained that 100 beneficiaries on the basis of 50% for each racial group were targeted for the project.


Me Ramona told the meeting that they were experiencing difficulties in reaching the required numbers for the whites and that they have opted to get the remaining 13 beneficiaries from Hennenman. She said that the remaining 10 beneficiaries for blacks will be finalized by the end of the week, 08 September 2017.

- That Beneficiary management section to finalize the remaining 10 black beneficiaries by 8 September 2017.
- That beneficiary management section to request assistance from Speaker's to source the remaining 13 white beneficiaries from Hennenman.

	She indicated that they have not yet filled forms for beneficiaries because beneficiaries must first be allocated sites.  Mr. Saru expressed disappointment that the information Me Ramona was providing is the same information provided to Human Settlements in August 2017 and that there seem to be no improvement in that regard.  Mr. Nieuwouldt suggested that in light of the challenges of land readiness and shortage of beneficiaries insito be considered as an alternative option.  House plans  Mr. Mohlabane raised the issue of beneficiaries having to choose the house plans as soon as possible.  The contractor indicated that 3 different house plans have been submitted for approval. The town planner insisted that there must be a plan submitted for each house to be built.	•	That Mr. Mohlabane to brief the HOD about the challenges of land readiness and shortage of beneficiaries for the HOD to apply his mind.  That a recommendation to be made for consideration to go insito, preferably in Mmamahabane to further check the status of the land.  That beneficiaries to choose a plan only after the HOD has applied his mind.
5.4	It was confirmed that subdivision for 100 sites has been completed however the pegs and maps were still outstanding.  It was also notice that the township register has not been opened and that would take approximately six months to get it approved if funds are available.	•	That a surveyor to be appointed to peg the subdivided sites if funds are available.  That Mr. Boipelo to ensure that maps and drawings are finalized.
6.	CLOSURE  Mr. Mohlabane thanked everyone for fruitful engagements and for responding positive to the invitation at such a short notice.  The meeting adjourned at 14h00		

#### GENERAL PLAN OF VARIOUS ERF SUBDIVISIONS VENTERSBURG EXTENSION 6.

#### SCALE 1: 500

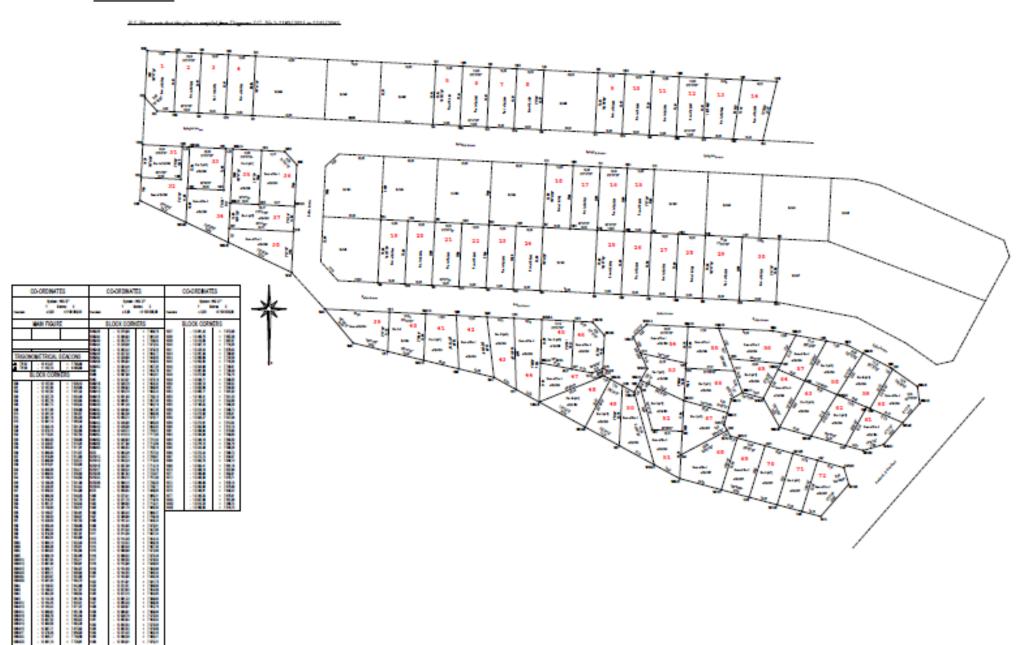

### VENTERSBURG: EXTENSION 6: SUBDIVISION OF ERVEN

#### **Town Planning aspects:**

- Subdivision plan was approved 72 subdivided erven were created (Layout plan is attached)
- Area was surveyed and registered by the Surveyor General
- Cadastral information is available at Infrastructure Directorate.
- Cadastral information already provided to the contractor.

#### **Infrastructure: Engineering services:**

- Internal services All services are available but has been lying unutilized for a long time and therefore have to be cleaned (Estimated cost R2 million and will take approximately 3 months)
- Erf Connections All new erven must be connected to the internal reticulation networks (Approximately R10 000 per site R 720 000)
- Bulk Services: All bulk services are available.

#### **Infrastructure: Electrical Services:**

Information to be provided by the Electrical Engineer

DAS Operator: John Jakobs

Voltage 11 kV Ventersburg

**Transmission** 

NMD Next recom:

Next ver:

2008

	2010	2011	2012	2013	2014	2015	2016	2017
Jan	450876	487528	483760	471121	462739	434815	437 604.00	431458
Feb	417170	452979	447076	430261	409836	391587	409 863.00	397293
Mar	461414	488227	467975	458175	438991	433370	419 634.00	439006
Apr	441483	483877	453462	447670	426435	408500	413 921.00	420656
May	503265	558418	491804	500358	465592	436509	458 895.00	487982
Jun	581225.4	610251	582003	548225	506700	511462	497 422.00	528929
Jul	605082	646122	612254	555485	556784	542046	534 024.00	530625
Aug	575793	590316	571235	542565	502217	498362	497 453.00	529843
Sep	485103	473400	472660	462409	438822	441208	419 914.00	
Oct	490358	475016	459700	459017	432469	438183	433585	
Nov	465410	456803	455859	444152	399849	417903	422566	
Dec	488695	477364	467594	441967	429703	452629	442587	

	2010	2011	2012	2013	2014	2015	2016	2017	NMD
	1	1		1		1			
Jan	096.85	090.94	964.10	289.44	900.13	024.11	930.98	847.25	1200
	1	1							
Feb	172.15	103.00	962.23	925.23	916.36	875.02	857.73	859.59	1200
	1	1			1		1		
Mar	151.20	260.55	965.45	961.29	132.73	878.09	007.32	859.36	1200
	1	1				1			
Apr	091.26	157.77	978.41	989.85	953.35	106.99	896.72	875.00	1200
	1	1	1	1	1	1			
May	113.28	207.56	036.07	054.54	089.81	033.46	908.95	994.04	1200

	1	1	1	1	1	1	1	1	
Jun	357.66	340.16	267.67	162.58	052.72	310.45	044.93	106.14	1200
	1	1	1	1	1	1	1	1	
Jul	321.53	324.95	230.69	158.24	118.83	115.12	149.18	039.94	1200
	1	1	1	1	1	1	1	1	
Aug	278.52	261.29	338.91	149.35	003.88	146.84	052.37	044.99	1200
	1	1	1	1					
Sep	373.10	019.73	048.17	208.48	934.71	913.23	839.96		1200
	1								
Oct	292.11	983.24	937.00	907.17	893.04	859.22	877.38		1200
	1		1						
Nov	123.33	964.78	207.98	918.19	852.80	853.19	877.51		1200
	1			1					
Dec	098.75	979.64	949.09	085.16	993.95	927.57	887.51		1200

#### Revenue

	2012	2013	2014	2015	2016	2017	Forecast
Jan	257940.74	325268.17	353896.88	374687.39	420905.91	438324.19	
Feb	246796.21	263908.04	325379.32	333975.64	393501.34	413946.81	
Mar	253418.17	277536.75	361074.58	357793.96	416740.6	445407.43	
Apr	250474.66	277449.02	338102.13	366528.99	400640.88	433418.35	
May	268068.36	302523.97	372261.62	376610.84	433302.69	497969.07	
Jun	500132.67	515884.19	534563.98	593688.58	647512.24	740565.76	
Jul	560856.36	584200.97	626419.8	700642.13	754857.7	729633.95	
Aug	565523.47	584735.19	562951.39	670574.28	700159.62	730056.61	
Sep	292619.39	380899.84	368533.3	421408.65	428740.32		
Oct	275134.84	352423	360746.59	413482.22	443463		
Nov	306518.52	344973.08	336957.23	398661.39	435145.53		
Dec	279170.61	358547.56	368697.37	430977.89	451403.39		

Matjhabeng Ventersburg Electricity

> Scale n.t.s. 05-09-2017

> > NOTES:

Generalised Zoning

Detailed Zoning obtainable from Spatial Planning







